etereo ARCHITECTURE&DESIGN&EMOTION	Eng. Adnan Saffarini Office Architects & Engineering Consultants	GUIDELINE INTERIORS

Page 1 of 1	Doc Ref.:	EAS-DT	Form sheet Title:	**Document Transmittal**

Transmittal No.	EAS-GLI-DT-001	Rev.	02	Date	Monday, 13 February 2023

Project Title	AL SAFIYA PALACE	Plot No.	0506
Employer Name	M/S AQAAR – AJMAN PROPERTIES CORPORATION	Location	AJMAN, UAE
Subject			

Transmitted to	Mr.	**From**	Mr.
Company	M/s Eng. Adnan Saffarini Office (EAS)	Company	M/s Guideline Interiors LLC
Location	Ajman Branch	Location	Dubai Silicon Oasis
Phone No.	067441101	Phone No.	043922240
Fax No.		Fax No.	043922250
Email	easajman@saffarinidxb.com	Email	projects@guideline.ae

List of Drawings / Documents Details:

Item	Drawings / Documents / Submittal Ref.	REV.	Format	No. of Copies	Description
1.	PROGRAMME OF WORK	02	Soft Copy	1	PROGRAMME OF WORK
2.	GROUND ZONE PLAN	01	Soft Copy	1	GROUND ZONE PLAN
3.	FIRST ZONE PLAN	01	Soft Copy	1	FIRST ZONE PLAN
4.	TERRACE ZONE PLAN	01	Soft Copy	1	TERRACE ZONE PLAN

Reason for Submittal

- ☐ As Requested
- ☐ For your Information & Record.
- ☑ For your Approval
- ☐ For your Comments
- ☐ Additional Copies
- ☐ For Urgent Action
- ☐ For Forwarding Sub-Contractor
- ☐ For Construction

Issued By Contractor

Name: ENGR. JOSEPH FELIX

Signature: _____

Date: 13 / 02 / 2023 Time: 10 : 20 PM/ **AM**

Received by Consultant

Name: _____

Signature: _____

Date: / / 20 Time: ____:____ PM/ AM

Consultant's Comments (Project Manager / Resident Engineer)

1.Completion of project should be as per contract days. 2.I.D contractor should include all the materials as per approved quotation & procurement schedule should cover all the major items. 3.Manpower histogram & cash flow chart should be attached with the program. 4.No objection for proposed zone plans, Main contractor & I.D contractor to coordinate with zone plans clearance, then submit to consultant for approval.

Approval Status:

- ☐ Approved
- ☑ Approved As noted
- ☐ Revise and Re-Submit
- ☐ Rejected

Name of Consultant's Representative:

Eng. Meer Hussain

Signature: Muth

Date: 16 / 02 / 20 23 Time: ____:____ PM/ AM

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
Al Safya Palace Extension		19-Jan-23	30-Nov-23	262
Milestones & Prelims		19-Jan-23	03-Feb-2	14
A1000	Contract Signing	19-Jan-23		0
A1010	Advanced Payment	19-Jan-23		0
A1020	Kick-off Meeting	19-Jan-23		0
A1030	Porto Cabin Installation	19-Jan-23	26-Jan-23	7
A1040	Service connections	19-Jan-23	26-Jan-23	7
A3430	Mobilazation	19-Jan-23	03-Feb-2	14
Engineering		04-Feb-23	22-May-2	89
A1050	Shop Drawings Submittal	04-Feb-23	05-May-2	75
A1060	Shop Drawings Aproval	15-Feb-23	11-May-2	70
A1070	Samples Submittal	04-Feb-23	15-May-2	82
A1080	Samples Approval	08-Feb-23	22-May-2	86
Procurement		06-Feb-23	01-Nov-2	222
Production		06-Feb-23	20-Oct-23	212
A5078	Steel structure for the staircase	22-Mar-23	03-Jun-23	60
A5079	Purchasing screed		08-Feb-2	0
A5080	Screed material	15-Feb-23	23-Feb-2	7
A5089	Purchasing suspension & supporting materia		06-Feb-2	0
A5090	Suspension and supporting items	08-Feb-23	18-Feb-2	10
A5099	Purchasing GBs		06-Feb-2	0
A5100	Gypsum boards (normal & MR)	08-Feb-23	18-Feb-2	10
A5101	Purchasing marble		08-Mar-2	0
A5102	Marble	24-Feb-23	13-Jun-23	90
A5103	Purchasing porcelain		15-Mar-2	0
A5104	Porcelain	08-Mar-23	20-May-2	60
A5105	Purchasing metals		20-Mar-2	0
A5106	Metal (claddings, ceiling and walls profiles)	14-Mar-23	20-Oct-23	180
A5107	Purchasing paints		20-Mar-2	0
A5108	Paints	14-Mar-23	06-Apr-23	20
A5109	Purchasing ceiling tiles		16-Feb-2	0
A5110	Ceiling Tiles	13-Feb-23	08-Mar-2	20
A5119	Purchasing glass		01-Apr-23	0
A5470	Glass	31-Mar-23	28-Aug-2	120
A7659	Purchasing wooden raw materials		24-Apr-23	0
A7660	Wooden raw materials (solid wood, MDF,..e	11-May-23	23-May-2	10
A7669	Purchasing wooden finishes		27-Apr-23	0
A7670	Wooden finsihes (veneer,laminate,...etc)	11-May-23	26-Jul-23	60
A7679	Purchasing joinery accessories		01-Jul-23	0
A7680	Joinery accessories (handels,hinges,drawer	26-Jul-23	30-Aug-2	30
A7688	Purchasing doors accessories		08-Jul-23	0
A7689	Doors accessories (handels,hinges,lock,cyinc	25-Jul-23	29-Aug-2	30
A7690	Purchasing wallpaper		24-Apr-23	0
A7691	Wallpaper	18-Apr-23	11-Jul-23	65
A7692	Purchasing leather fabrics		01-May-2	0
A7693	Leather fabrics	03-May-23	16-Aug-2	85
A7694	Purchasing mirrors		13-Mar-2	0
A7695	Mirrors	14-Mar-23	12-Apr-23	25
A7696	Purchasing parquet		16-Mar-2	0
A7697	Parquet	14-Mar-23	05-Jul-23	90

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
A7698	Purchasing carpet		15-May-2	0
A7699	Carpet	15-May-23	19-Jun-23	30
Delivery		18-Feb-23	01-Nov-2	210
A4969	Steel structure material "SITE"	03-Jun-23	15-Jun-23	10
A4970	Screed material "SITE"	23-Feb-23	03-Mar-2	7
A4980	Suspension and supporting items "SITE"	18-Feb-23	24-Feb-2	5
A4990	Gypsum boards (normal & MR) "SITE"	18-Feb-23	24-Feb-2	5
A4991	Marble "FACTORY"	31-Mar-23	24-Jul-23	90
A4992	Porcelain "SITE"	20-May-23	07-Jun-23	15
A4993	Metal (claddings, ceiling and walls profiles) '	20-Oct-23	01-Nov-2	10
A4994	Paints "SITE"	06-Apr-23	12-Apr-23	5
A4995	Ceiling Tiles "SITE"	08-Mar-23	14-Mar-2	5
A4996	Glass "FACTORY"	28-Aug-23	08-Sep-2	10
A6290	Wooden raw materials (solid wood, MDF,..e	23-May-23	29-May-2	5
A6300	Wooden finsihes (veneer,laminate,...etc) 'FA	26-Jul-23	01-Aug-2	5
A6780	Joinery accessories (handels,hinges,drawer	30-Aug-23	11-Sep-2	10
A6860	Doors accessories (handels,hinges,lock,cyinc	29-Aug-23	09-Sep-2	10
A6861	Wallpaper "FACTORY"	11-Jul-23	24-Jul-23	10
A6862	Leather fabrics "FACTORY"	16-Aug-23	28-Aug-2	10
A6863	Mirrors "FACTORY"	12-Apr-23	27-Apr-23	10
A6864	Parquet "SITE"	05-Jul-23	29-Jul-23	20
A6865	Carpet "FACTORY"	19-Jun-23	24-Jun-23	5
Construction		14-Feb-23	30-Nov-2	240
A4960	Snagging & De-snagging	27-Oct-23	30-Nov-2	30
A5040	Staircase steel structure installation	15-Jun-23	26-Jul-23	30
Ground Floor		14-Feb-23	30-Nov-2	240
A7070	MEP Clearance of all flooring items		28-Feb-2	0
A7080	Screed Works	03-Mar-23	21-Mar-2	15
Zone A		14-Feb-23	30-Nov-2	240
A7359	MEP Clearence (ceiling suspension)		14-Feb-2	0
A7360	Plastering & anyother related civil works		21-Feb-2	0
Ceiling		15-Feb-23	18-Nov-2	228
A7370	Supporting & suspension system installation	15-Feb-23	10-Mar-2	20
A7379	Clearence for ceiling closing		13-Mar-2	0
A7380	Gypsum boards installation	14-Mar-23	06-Apr-23	20
A7390	Bulkheads & curtain boxes	31-Mar-23	18-Apr-23	15
A7400	Finishing and Painting works	18-Apr-23	09-May-2	15
A7450	Brushed metal profiles installation	01-Nov-23	18-Nov-2	15
Walls		25-Mar-23	24-Nov-2	201
A7409	Walls Clearence		25-Mar-2	0
A7410	Supporting system	25-Mar-23	18-Apr-23	20
A7420	Gypsum cladding	04-Apr-23	25-Apr-23	15
A7430	Marble cladding	09-May-23	13-Jun-23	30
A7460	Skirting installation	13-Jul-23	26-Jul-23	10
A7470	Metal profiles installation	01-Nov-23	24-Nov-2	20
A7510	Finishing & painting works	07-Jun-23	24-Jun-23	15
Flooring		08-May-23	13-Jul-23	54
A7479	Flooring Clearence		08-May-2	0
A7480	Flooring preparations	09-May-23	17-May-2	7
A7490	Self-leveling	17-May-23	03-Jun-23	15
A7500	Marble fooring installation	03-Jun-23	13-Jul-23	30

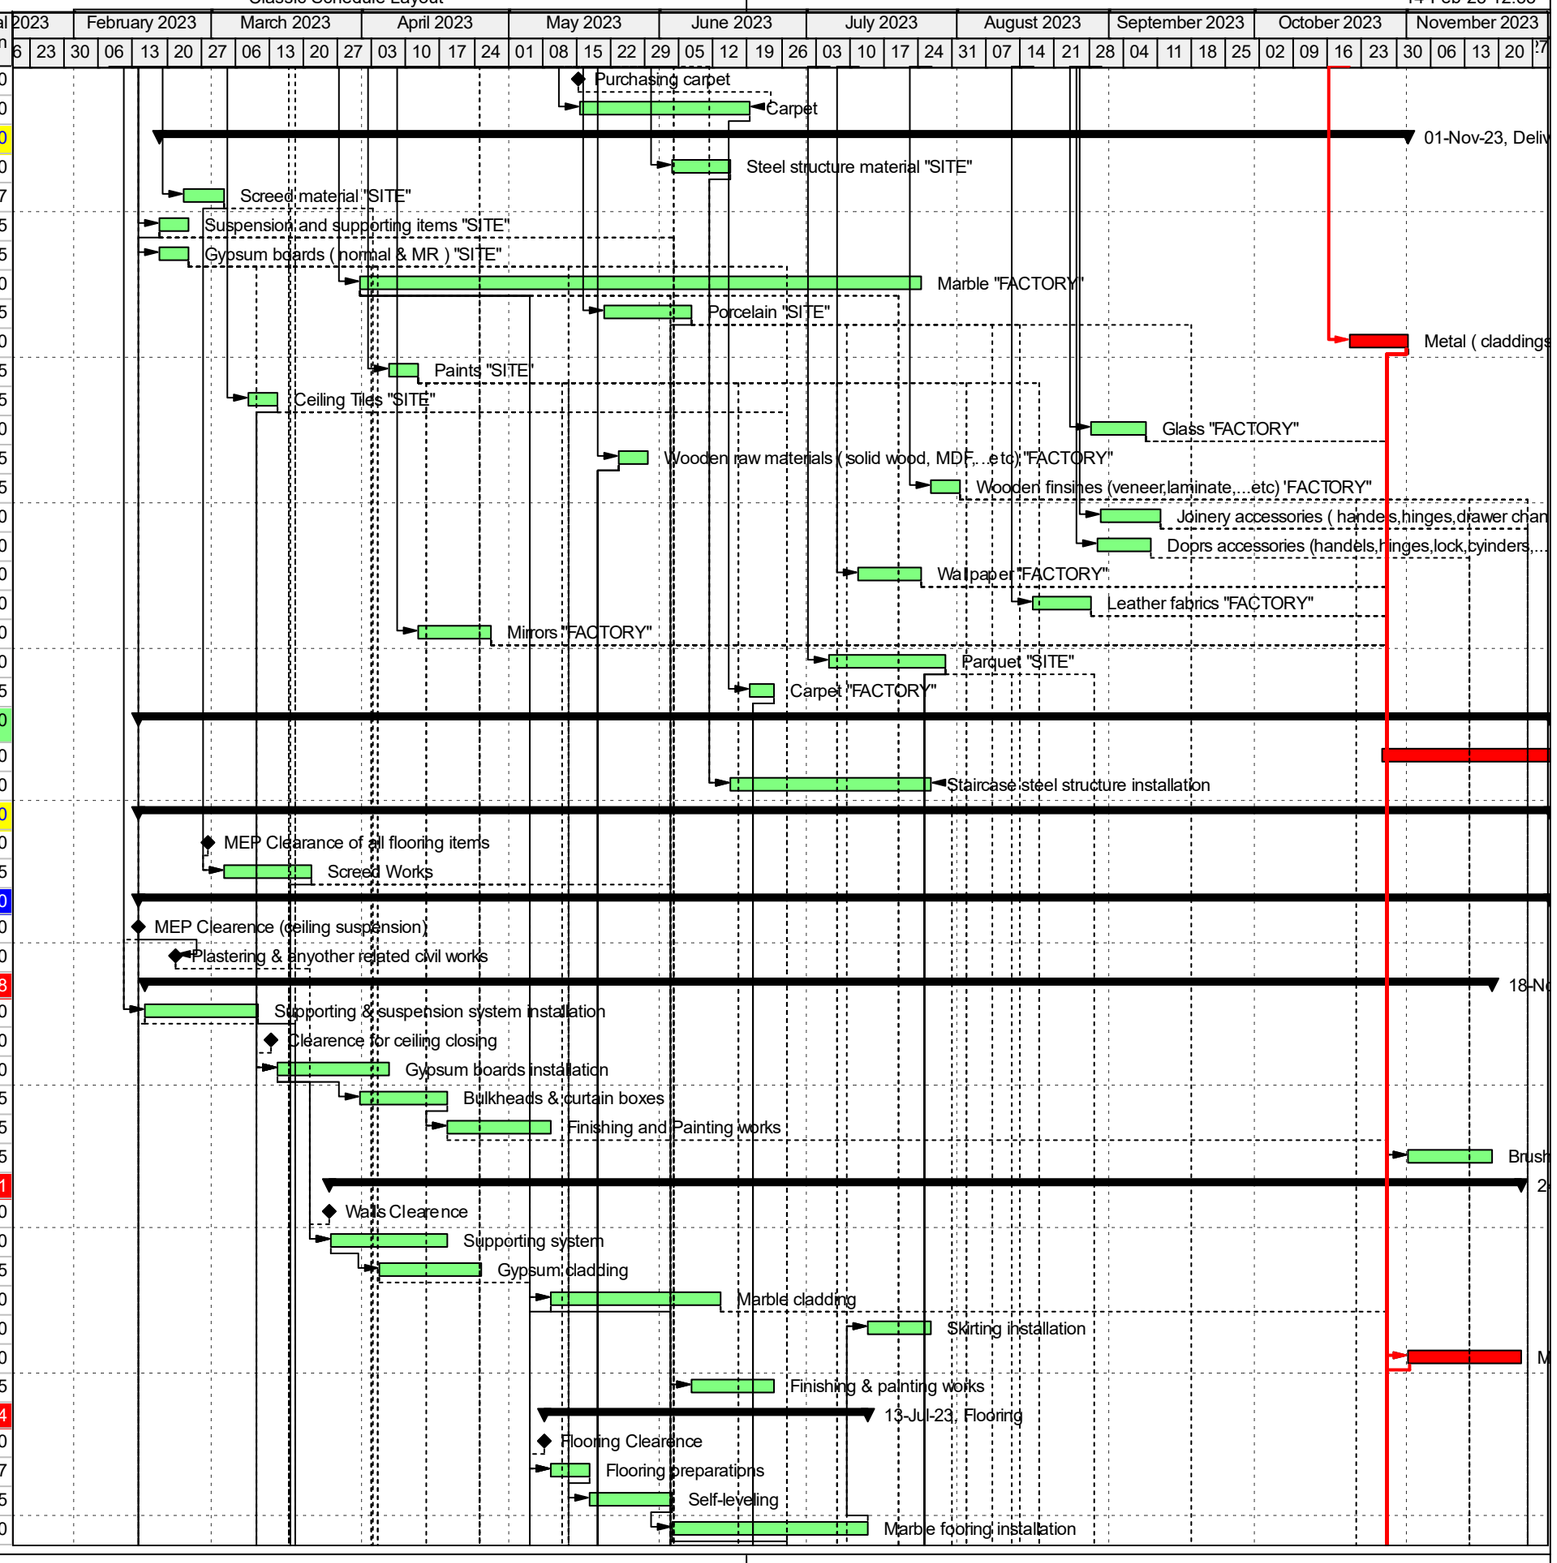

Actual Work | Remaining Work | Critical Remaining Work | Summary | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
Special Items & Joinery preparations		07-Jun-23	30-Nov-2	145
A7520	Joinery items sub structures and general pre	01-Jul-23	19-Jul-23	15
A7530	Mirrors installation	01-Nov-23	30-Nov-2	25
A7540	Doors sub frames	10-Jul-23	22-Jul-23	10
A7550	Parquet flooring	29-Jul-23	04-Aug-2	5
A7560	Leather cladding	01-Nov-23	24-Nov-2	20
A7570	Porcelain flooring	07-Jun-23	13-Jun-23	5
Zone B		21-Mar-23	30-Nov-2	210
A7120	MEP Clearence (ceiling suspension)		21-Mar-2	0
A7130	Plastering & anyother related civil works		30-Mar-2	0
Ceiling		22-Mar-23	18-Nov-2	198
A7140	Supporting & suspension system installation	22-Mar-23	14-Apr-23	20
A7149	Clearence for ceiling closing		07-Apr-23	0
A7150	Gypsum boards installation	08-Apr-23	05-May-2	20
A7160	Bulkheads & curtain boxes	29-Apr-23	17-May-2	15
A7170	Finishing and Painting works	17-May-23	03-Jun-23	15
A7220	Brushed metal profiles installation	01-Nov-23	18-Nov-2	15
Walls		24-Apr-23	24-Nov-2	179
A7179	Walls Clearance		24-Apr-23	0
A7180	Supporting system	24-Apr-23	17-May-2	20
A7190	Gypsum cladding	03-May-23	20-May-2	15
A7200	Marble cladding	09-May-23	13-Jun-23	30
A7230	Skirting installation	13-Jul-23	26-Jul-23	10
A7240	Metal profiles installation	01-Nov-23	24-Nov-2	20
A7280	Finishing & painting works	07-Jun-23	24-Jun-23	15
Flooring		08-May-23	13-Jul-23	54
A7249	Flooring clearence		08-May-2	0
A7250	Flooring preparations	09-May-23	17-May-2	7
A7260	Self-leveling	17-May-23	03-Jun-23	15
A7270	Marble fooring installation	03-Jun-23	13-Jul-23	30
Special Items & Joinery preparations		24-Jun-23	30-Nov-2	130
A7290	Joinery items sub structures and general pre	01-Jul-23	19-Jul-23	15
A7300	Mirrors installation	01-Nov-23	30-Nov-2	25
A7310	Doors sub frames	10-Jul-23	22-Jul-23	10
A7320	Parquet flooring	29-Jul-23	16-Aug-2	15
A7330	Leather cladding	01-Nov-23	24-Nov-2	20
A7340	Porcelain flooring	13-Jul-23	01-Aug-2	15
A7580	Carpet flooring	24-Jun-23	05-Jul-23	5
Zone C		27-Apr-23	30-Nov-2	181
A6870	MEP Clearence (ceiling suspension)		27-Apr-23	0
A6880	Plastering & anyother related civil works		05-May-2	0
Ceiling		29-Apr-23	24-Nov-2	173
A6890	Supporting & suspension system installation	29-Apr-23	23-May-2	20
A6899	Clearence for ceiling closing		17-May-2	0
A6900	Gypsum boards installation	17-May-23	09-Jun-23	20
A6910	Bulkheads & curtain boxes	03-Jun-23	21-Jun-23	15
A6920	Finishing and Painting works	21-Jun-23	13-Jul-23	15
A6970	Brushed metal profiles installation	01-Nov-23	24-Nov-2	20
Walls		26-May-23	24-Nov-2	151
A6929	Walls Clearence		26-May-2	0
A6930	Supporting system	29-May-23	21-Jun-23	20
A6940	Gypsum cladding	07-Jun-23	24-Jun-23	15

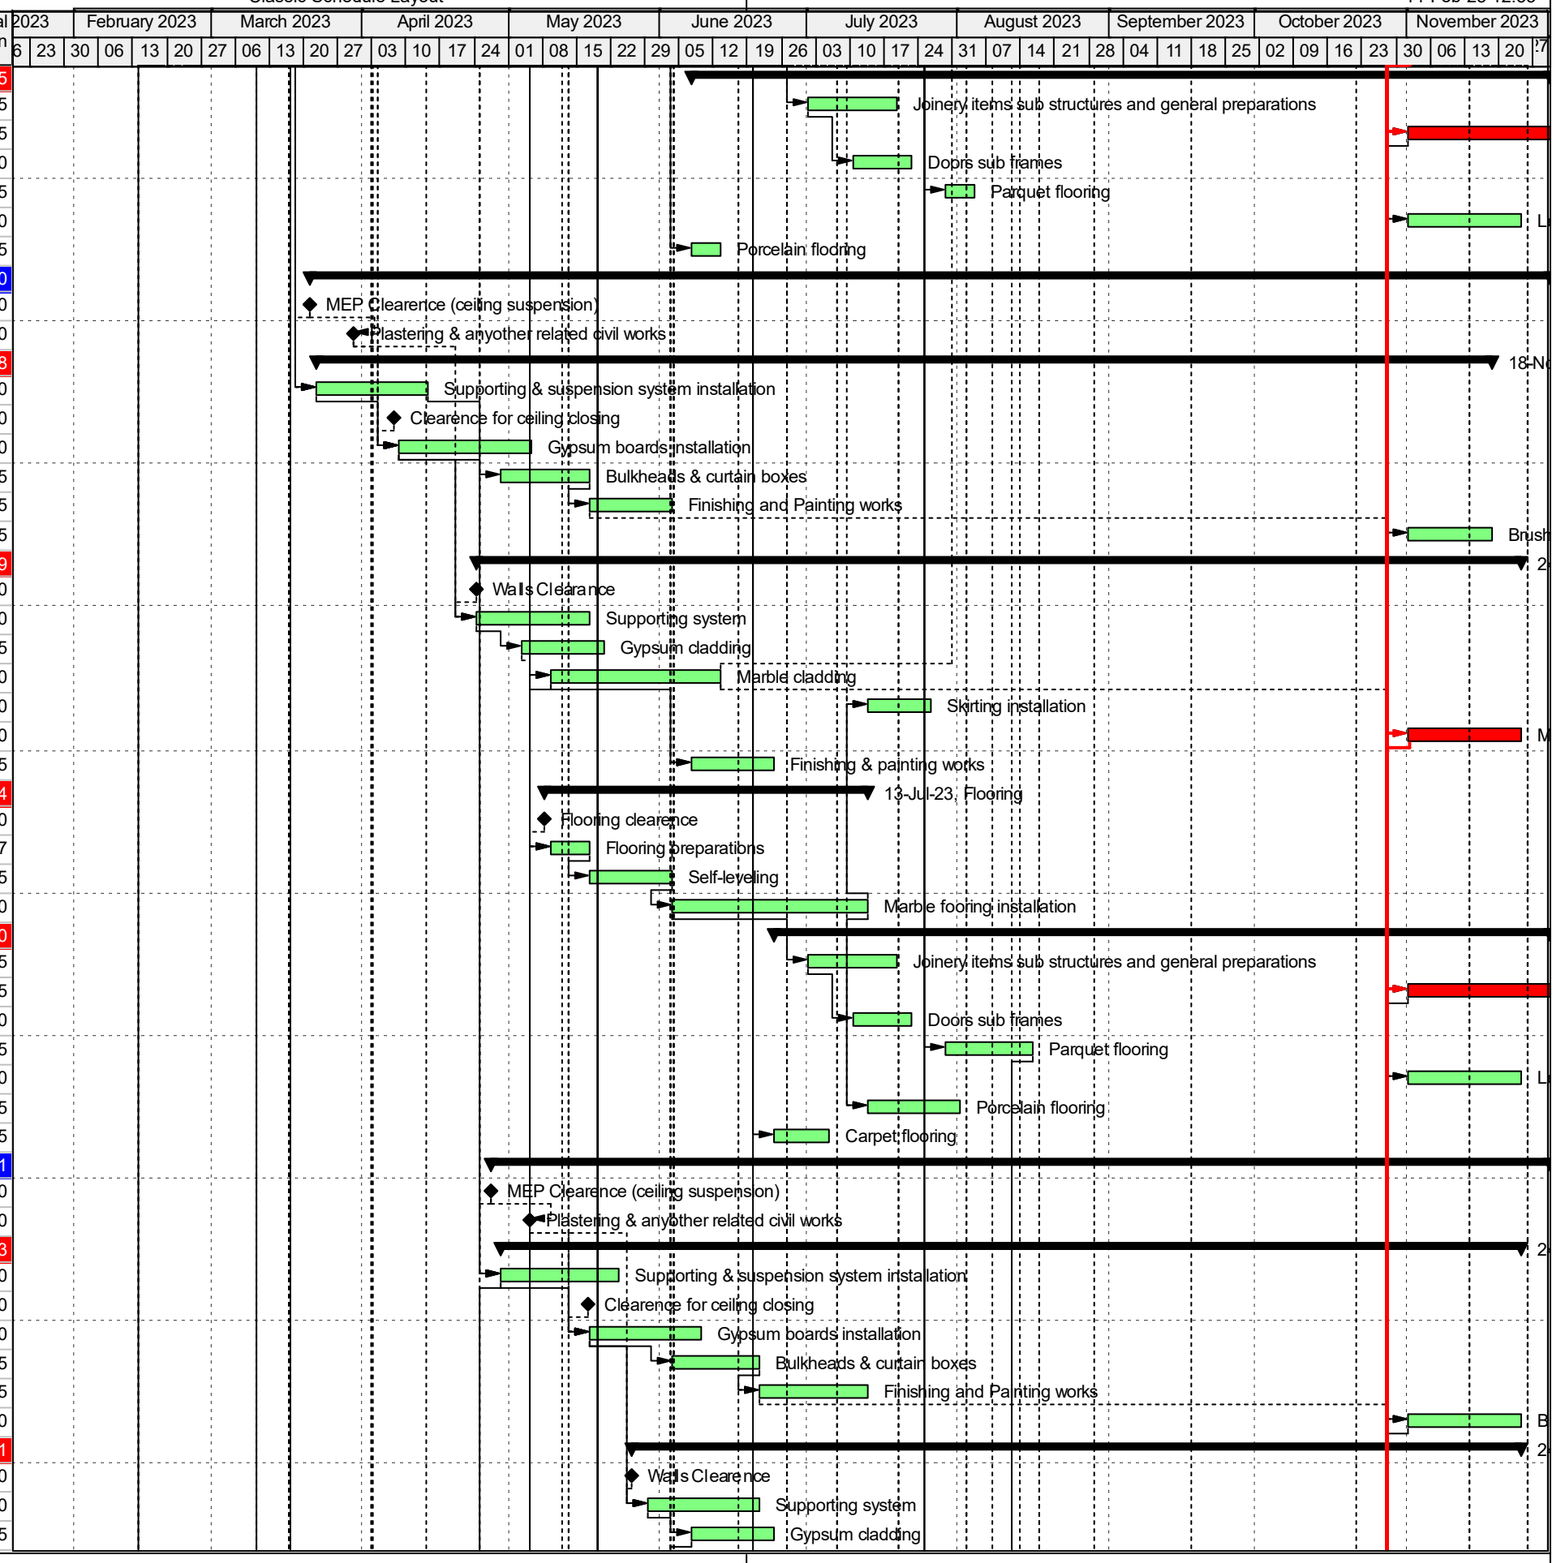

Actual Work | Remaining Work | Critical Remaining Work | Summary | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
A6950	Marble cladding	07-Jun-23	17-Jul-23	30
A6960	Wallpapers installation	01-Nov-23	18-Nov-2	15
A6980	Skirting installation	12-Aug-23	24-Aug-2	10
A6990	Metal profiles installation	01-Nov-23	24-Nov-2	20
A7030	Finishing & painting works	11-Jul-23	29-Jul-23	15
Flooring		05-Jun-23	12-Aug-2	55
A6999	Flooring Clearence		05-Jun-23	0
A7000	Flooring preparations	07-Jun-23	15-Jun-23	7
A7010	Self-leveling	15-Jun-23	07-Jul-23	15
A7020	Marble fooring installation	07-Jul-23	12-Aug-2	30
Special Items & Joinery preparations		01-Aug-23	30-Nov-2	103
A7040	Joinery items sub structures and general pre	01-Aug-23	18-Aug-2	15
A7050	Mirrors installation	01-Nov-23	30-Nov-2	25
A7060	Doors sub frames	09-Aug-23	01-Sep-2	20
A7090	Parquet flooring	16-Aug-23	02-Sep-2	15
Zone D (wet areas)		01-Jul-23	24-Nov-2	124
A7589	MEP works and water-proofing test clearanc		01-Jul-23	0
A7590	Ceiling MR gypsum works	01-Jul-23	18-Jul-23	15
A7600	Walls cladding	19-Jul-23	05-Aug-2	15
A7610	Flooring installation	07-Aug-23	23-Aug-2	15
A7620	Porcelain flooring	07-Aug-23	17-Aug-2	10
A7630	Glass partitions	01-Nov-23	18-Nov-2	15
A7640	Mirrors installation	01-Nov-23	18-Nov-2	15
A7650	Brushed metal profiles	01-Nov-23	24-Nov-2	20
First Floor		14-Feb-23	30-Nov-2	240
A6270	MEP Clearance of all flooring items		13-Mar-2	0
A6280	Screed Works	21-Mar-23	07-Apr-23	15
Zone A		14-Feb-23	30-Nov-2	240
A6559	MEP Clearence (ceiling suspension)		14-Feb-2	0
A6560	Plastering & anyother related civil works		22-Feb-2	0
Ceiling		18-Feb-23	18-Nov-2	225
A6570	Supporting & suspension system installation	18-Feb-23	14-Mar-2	20
A6579	Clearence for ceiling closing		13-Mar-2	0
A6580	Gypsum boards installation	14-Mar-23	06-Apr-23	20
A6590	Bulkheads & curtain boxes	31-Mar-23	18-Apr-23	15
A6600	Finishing and Painting works	18-Apr-23	09-May-2	15
A6650	Brushed metal profiles installation	01-Nov-23	18-Nov-2	15
Walls		25-Mar-23	24-Nov-2	201
A6609	Walls Clearence		25-Mar-2	0
A6610	Supporting system	25-Mar-23	18-Apr-23	20
A6620	Gypsum cladding	04-Apr-23	25-Apr-23	15
A6630	Marble cladding	09-May-23	13-Jun-23	30
A6660	Skirting installation	13-Jul-23	26-Jul-23	10
A6670	Metal profiles installation	01-Nov-23	24-Nov-2	20
A6710	Finishing & painting works	07-Jun-23	24-Jun-23	15
Flooring		08-May-23	13-Jul-23	54
A6679	Flooring Clearence		08-May-2	0
A6680	Flooring preparations	09-May-23	17-May-2	7
A6690	Self-leveling	17-May-23	03-Jun-23	15
A6700	Marble fooring installation	03-Jun-23	13-Jul-23	30
Special Items & Joinery preparations		01-Jul-23	30-Nov-2	128

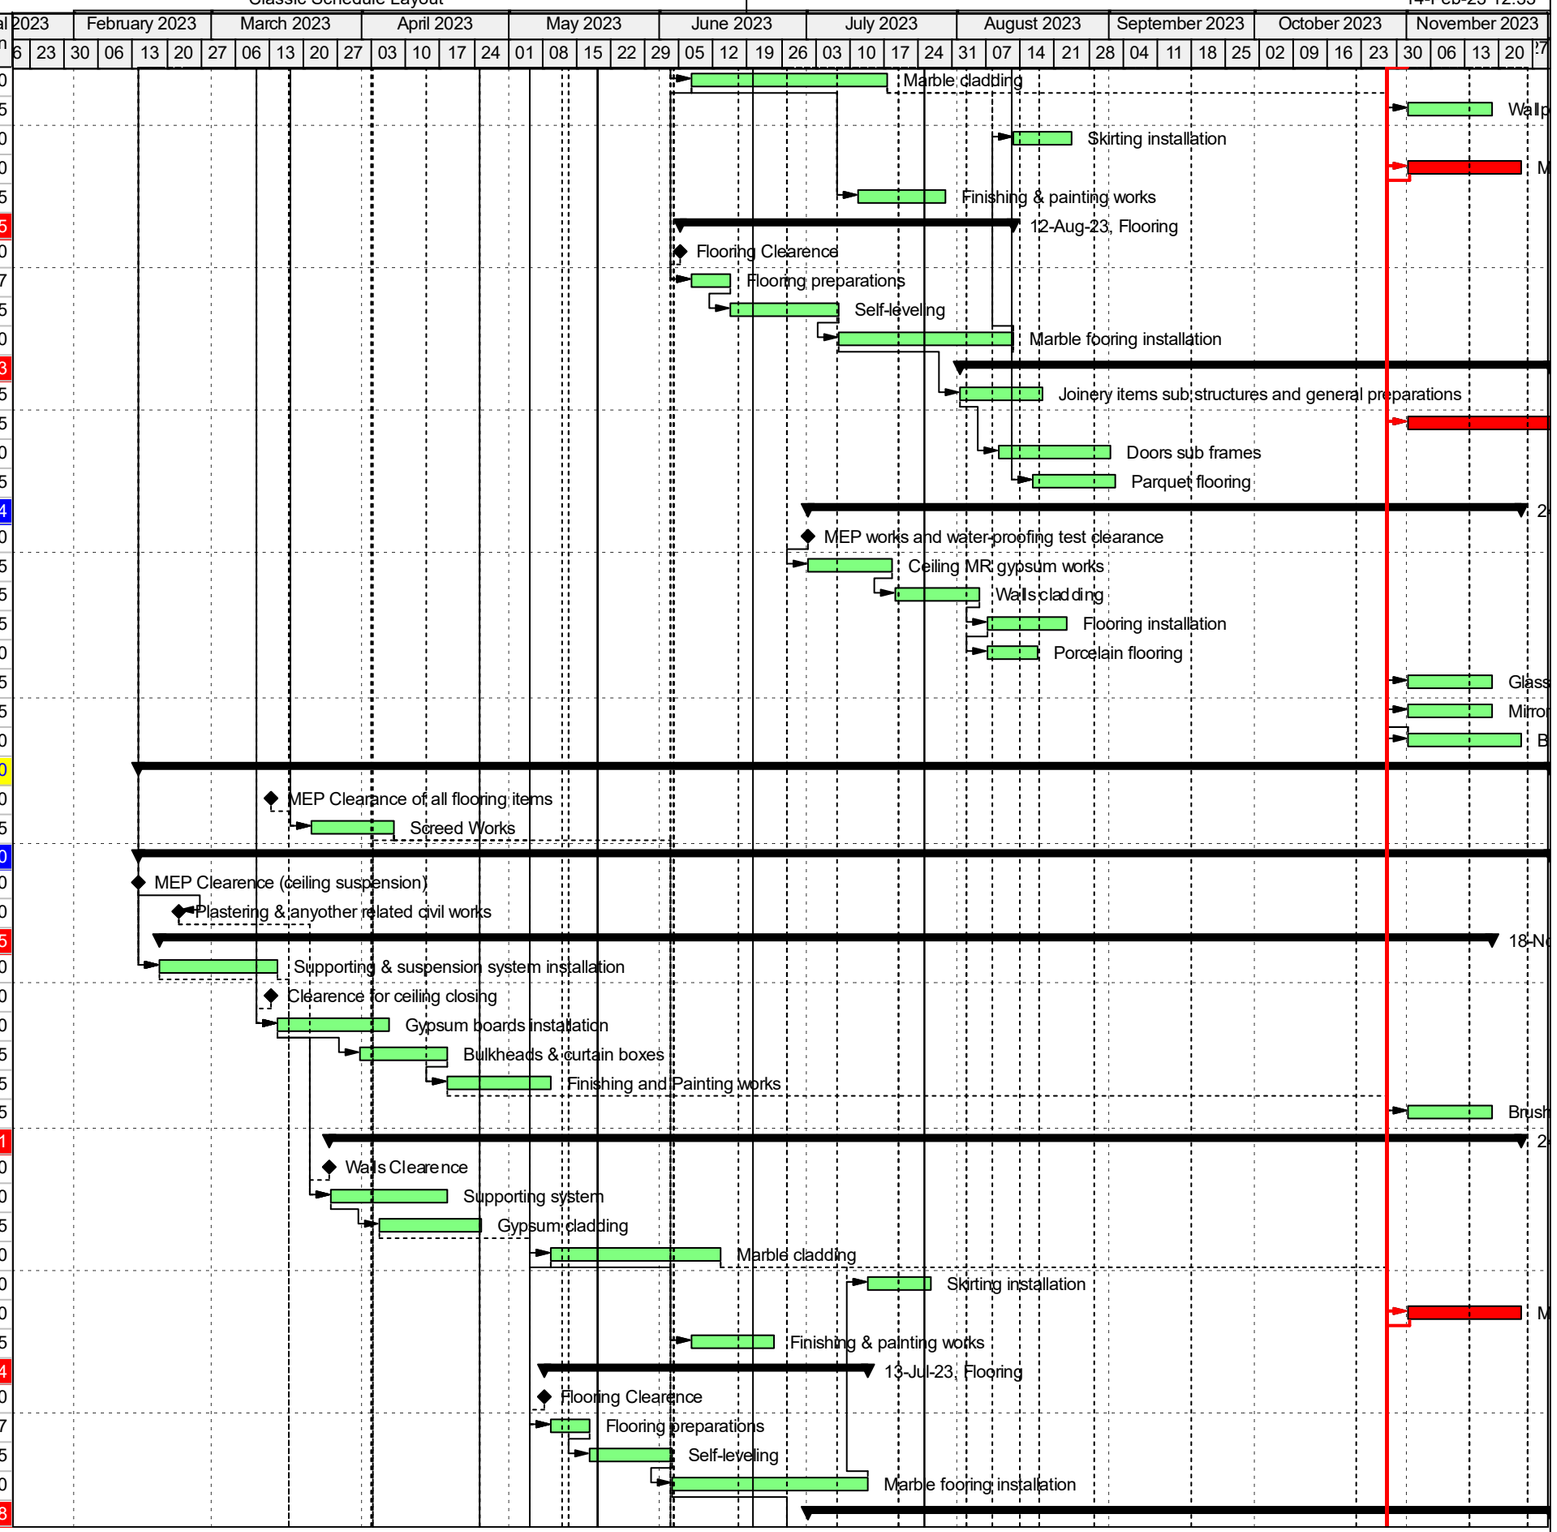

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
A6720	Joinery items sub structures and general pre	01-Jul-23	19-Jul-23	15
A6730	Mirrors installation	01-Nov-23	30-Nov-2	25
A6740	Doors sub frames	10-Jul-23	22-Jul-23	10
A6750	Parquet flooring	29-Jul-23	02-Sep-2	30
Zone B		21-Mar-23	30-Nov-2	210
A6329	MEP Clearence (ceiling suspension)		21-Mar-2	0
A6330	Plastering & anyother related civil works		03-Apr-23	0
Ceiling		21-Mar-23	30-Nov-2	210
A6340	Supporting & suspension system installation	21-Mar-23	12-Apr-23	20
A6349	Clearence for ceiling closing		07-Apr-23	0
A6350	Gypsum boards installation	07-Apr-23	03-May-2	20
A6360	Bulkheads & curtain boxes	28-Apr-23	15-May-2	15
A6370	Finishing and Painting works	16-May-23	01-Jun-23	15
A6420	Brushed metal profiles installation	01-Nov-23	30-Nov-2	25
Walls		24-Apr-23	24-Nov-2	179
A6379	Walls Clearence		24-Apr-23	0
A6380	Supporting system	24-Apr-23	16-May-2	20
A6390	Gypsum cladding	03-May-23	19-May-2	15
A6400	Marble cladding	09-May-23	13-Jun-23	30
A6410	Wallpapers installation	01-Nov-23	18-Nov-2	15
A6430	Skirting installation	13-Jul-23	26-Jul-23	10
A6440	Metal profiles installation	01-Nov-23	24-Nov-2	20
A6480	Finishing & painting works	07-Jun-23	24-Jun-23	15
Flooring		08-May-23	13-Jul-23	54
A6449	Flooring Clearence		08-May-2	0
A6450	Flooring preparations	09-May-23	17-May-2	7
A6460	Self-leveling	17-May-23	03-Jun-23	15
A6470	Marble fooring installation	03-Jun-23	13-Jul-23	30
Special Items & Joinery preparations		01-Jul-23	30-Nov-2	128
A6490	Joinery items sub structures and general pre	01-Jul-23	19-Jul-23	15
A6500	Mirrors installation	01-Nov-23	30-Nov-2	25
A6510	Doors sub frames	10-Jul-23	22-Jul-23	10
A6520	Parquet flooring	02-Sep-23	26-Sep-2	20
A6530	Leather cladding	01-Nov-23	24-Nov-2	20
Zone C		27-Apr-23	30-Nov-2	181
A6079	MEP Clearence (ceiling suspension)		27-Apr-23	0
A6080	Plastering & anyother related civil works		04-May-2	0
Ceiling		29-Apr-23	30-Nov-2	178
A6090	Supporting & suspension system installation	29-Apr-23	23-May-2	20
A6099	Clearence for ceiling closing		17-May-2	0
A6100	Gypsum boards installation	17-May-23	09-Jun-23	20
A6110	Bulkheads & curtain boxes	03-Jun-23	21-Jun-23	15
A6120	Finishing and Painting works	21-Jun-23	13-Jul-23	15
A6170	Brushed metal profiles installation	01-Nov-23	30-Nov-2	25
Walls		26-May-23	30-Nov-2	156
A6129	Walls Clearence		26-May-2	0
A6130	Supporting system	29-May-23	21-Jun-23	20
A6140	Gypsum cladding	07-Jun-23	24-Jun-23	15
A6150	Marble cladding	07-Jun-23	17-Jul-23	30
A6160	Wallpapers installation	01-Nov-23	30-Nov-2	25
A6180	Skirting installation	12-Aug-23	24-Aug-2	10

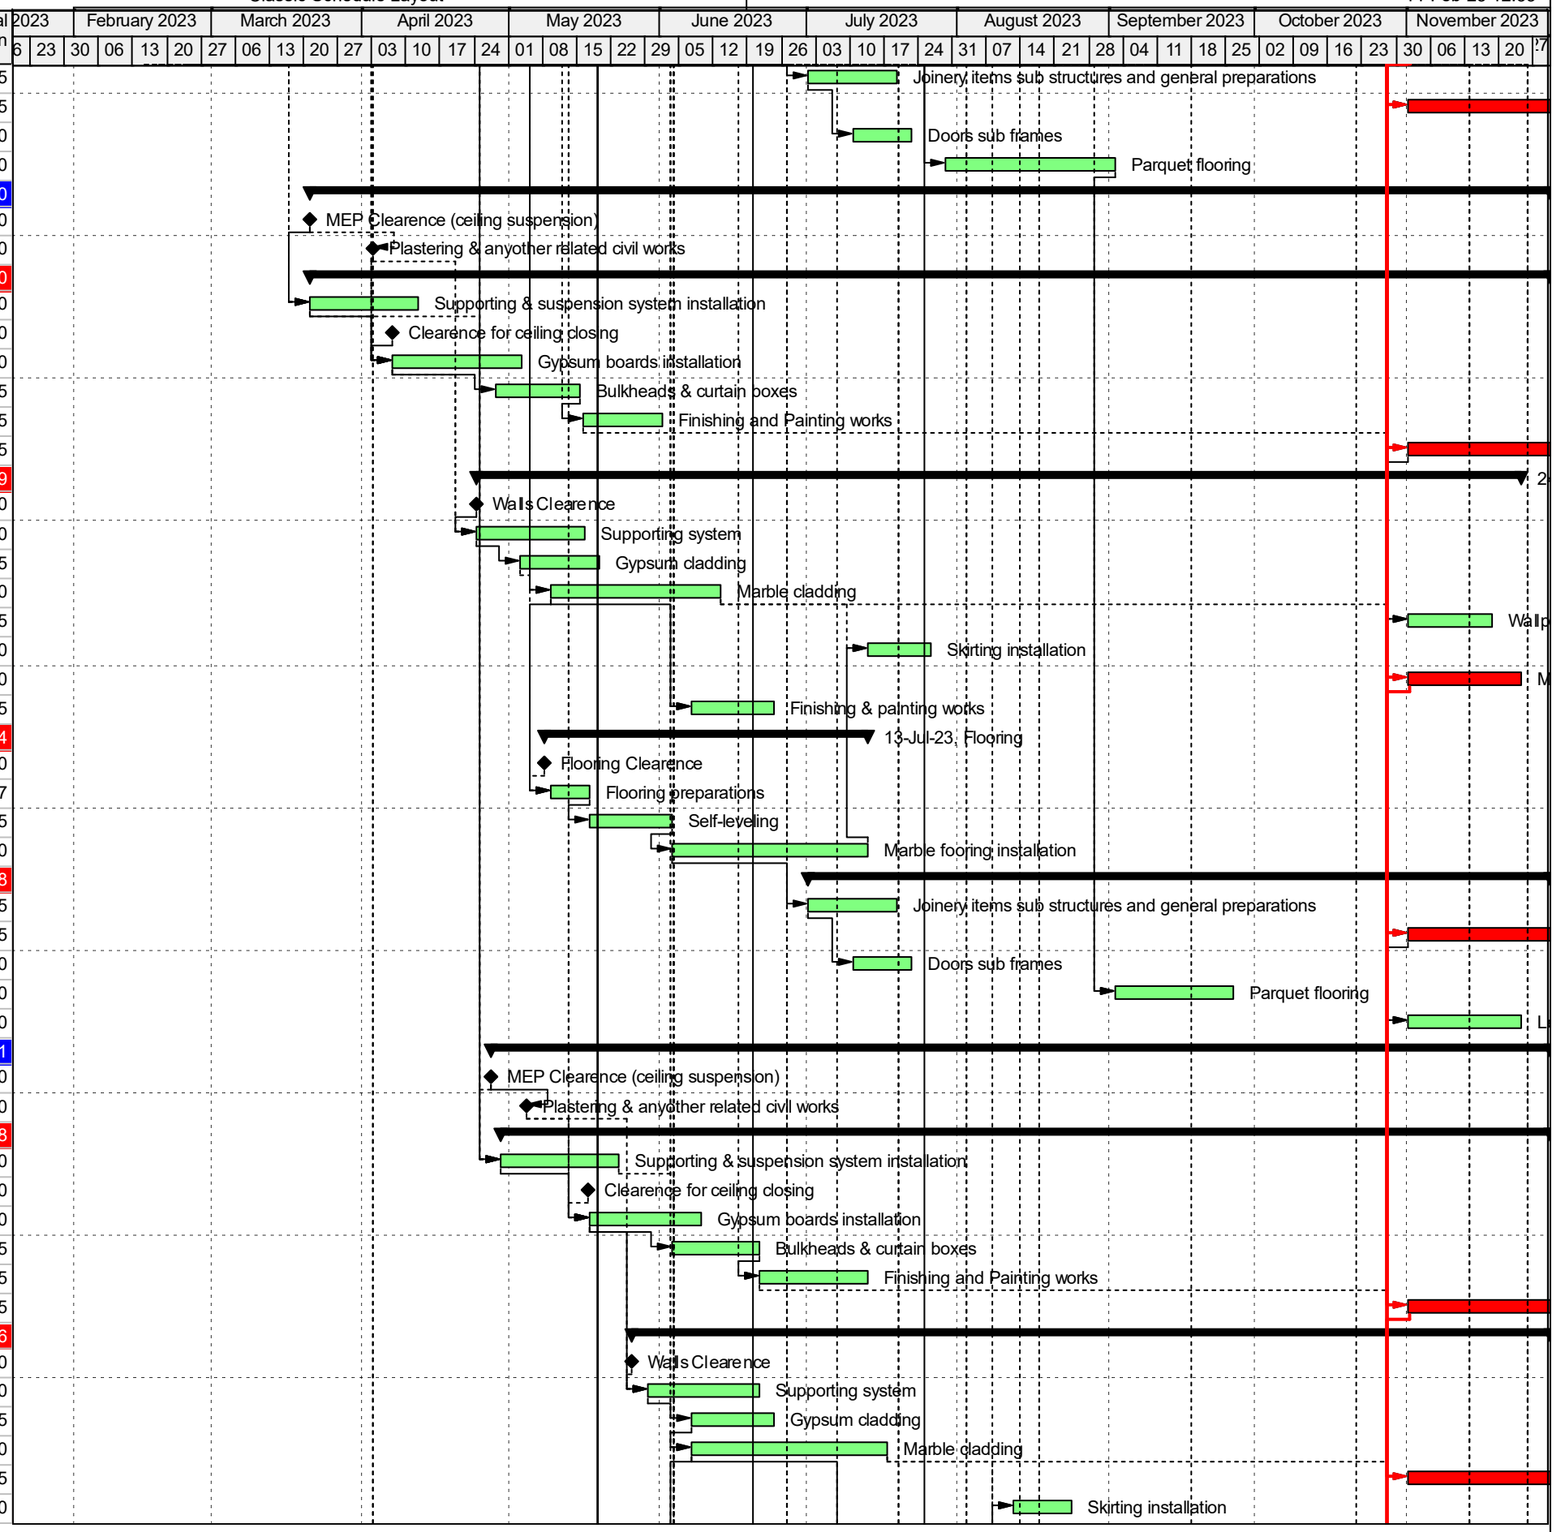

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
A6190	Metal profiles installation	01-Nov-23	30-Nov-2	25
A6230	Finishing & painting works	11-Jul-23	29-Jul-23	15
Flooring		05-Jun-23	12-Aug-2	55
A6199	Flooring Clearence		05-Jun-23	0
A6200	Flooring preparations	07-Jun-23	15-Jun-23	7
A6210	Self-leveling	15-Jun-23	07-Jul-23	15
A6220	Marble fooring installation	07-Jul-23	12-Aug-2	30
Special Items & Joinery preparations		01-Aug-23	28-Nov-2	101
A6240	Joinery items sub structures and general pre	01-Aug-23	18-Aug-2	15
A6250	Mirrors installation	01-Nov-23	28-Nov-2	23
A6260	Doors sub frames	09-Aug-23	21-Aug-2	10
A6310	Porcelain flooring	12-Aug-23	05-Sep-2	20
Zone D (wet areas)		22-Jul-23	24-Nov-2	107
A6789	MEP works and water-proofing test clearanc		22-Jul-23	0
A6790	Ceiling MR gypsum works	22-Jul-23	08-Aug-2	15
A6800	Walls cladding	09-Aug-23	25-Aug-2	15
A6810	Flooring installation	26-Aug-23	23-Sep-2	25
A6820	Porcelain flooring	26-Aug-23	18-Sep-2	20
A6830	Glass partitions	01-Nov-23	18-Nov-2	15
A6840	Mirrors installation	01-Nov-23	18-Nov-2	15
A6850	Brushed metal profiles	01-Nov-23	24-Nov-2	20
Terrace Floor		31-Mar-23	30-Nov-2	201
A4370	MEP Clearance of all flooring items		31-Mar-2	0
A4380	Screed Works	07-Apr-23	28-Apr-23	15
Zone A		08-Jun-23	30-Nov-2	145
A5769	MEP Clearence (ceiling suspension)		08-Jun-23	0
A5770	Plastering & anyother related civil works		15-Jun-23	0
Ceiling		08-Jun-23	18-Nov-2	135
A5780	Supporting & suspension system installation	08-Jun-23	05-Jul-23	20
A5789	Clearence for ceiling closing		01-Jul-23	0
A5790	Gypsum boards installation	01-Jul-23	25-Jul-23	20
A5800	Bulkheads & curtain boxes	19-Jul-23	05-Aug-2	15
A5810	Finishing and Painting works	07-Aug-23	23-Aug-2	15
A5860	Brushed metal profiles installation	01-Nov-23	18-Nov-2	15
Walls		12-Jul-23	24-Nov-2	115
A5819	Walls Clearence		12-Jul-23	0
A5820	Supporting system	13-Jul-23	05-Aug-2	20
A5830	Gypsum cladding	24-Jul-23	09-Aug-2	15
A5840	Marble cladding	24-Jul-23	26-Aug-2	30
A5870	Skirting installation	22-Sep-23	04-Oct-23	10
A5880	Metal profiles installation	01-Nov-23	24-Nov-2	20
A5920	Finishing & painting works	22-Aug-23	07-Sep-2	15
Flooring		20-Jul-23	21-Sep-2	54
A5889	Flooring Clearence		20-Jul-23	0
A5890	Flooring preparations	24-Jul-23	31-Jul-23	7
A5900	Self-leveling	01-Aug-23	17-Aug-2	15
A5910	Marble fooring installation	18-Aug-23	21-Sep-2	30
Special Items & Joinery preparations		18-Aug-23	30-Nov-2	89
A5930	Joinery items sub structures and general pre	11-Sep-23	27-Sep-2	15
A5940	Mirrors installation	01-Nov-23	30-Nov-2	25
A5950	Doors sub frames	19-Sep-23	30-Sep-2	10

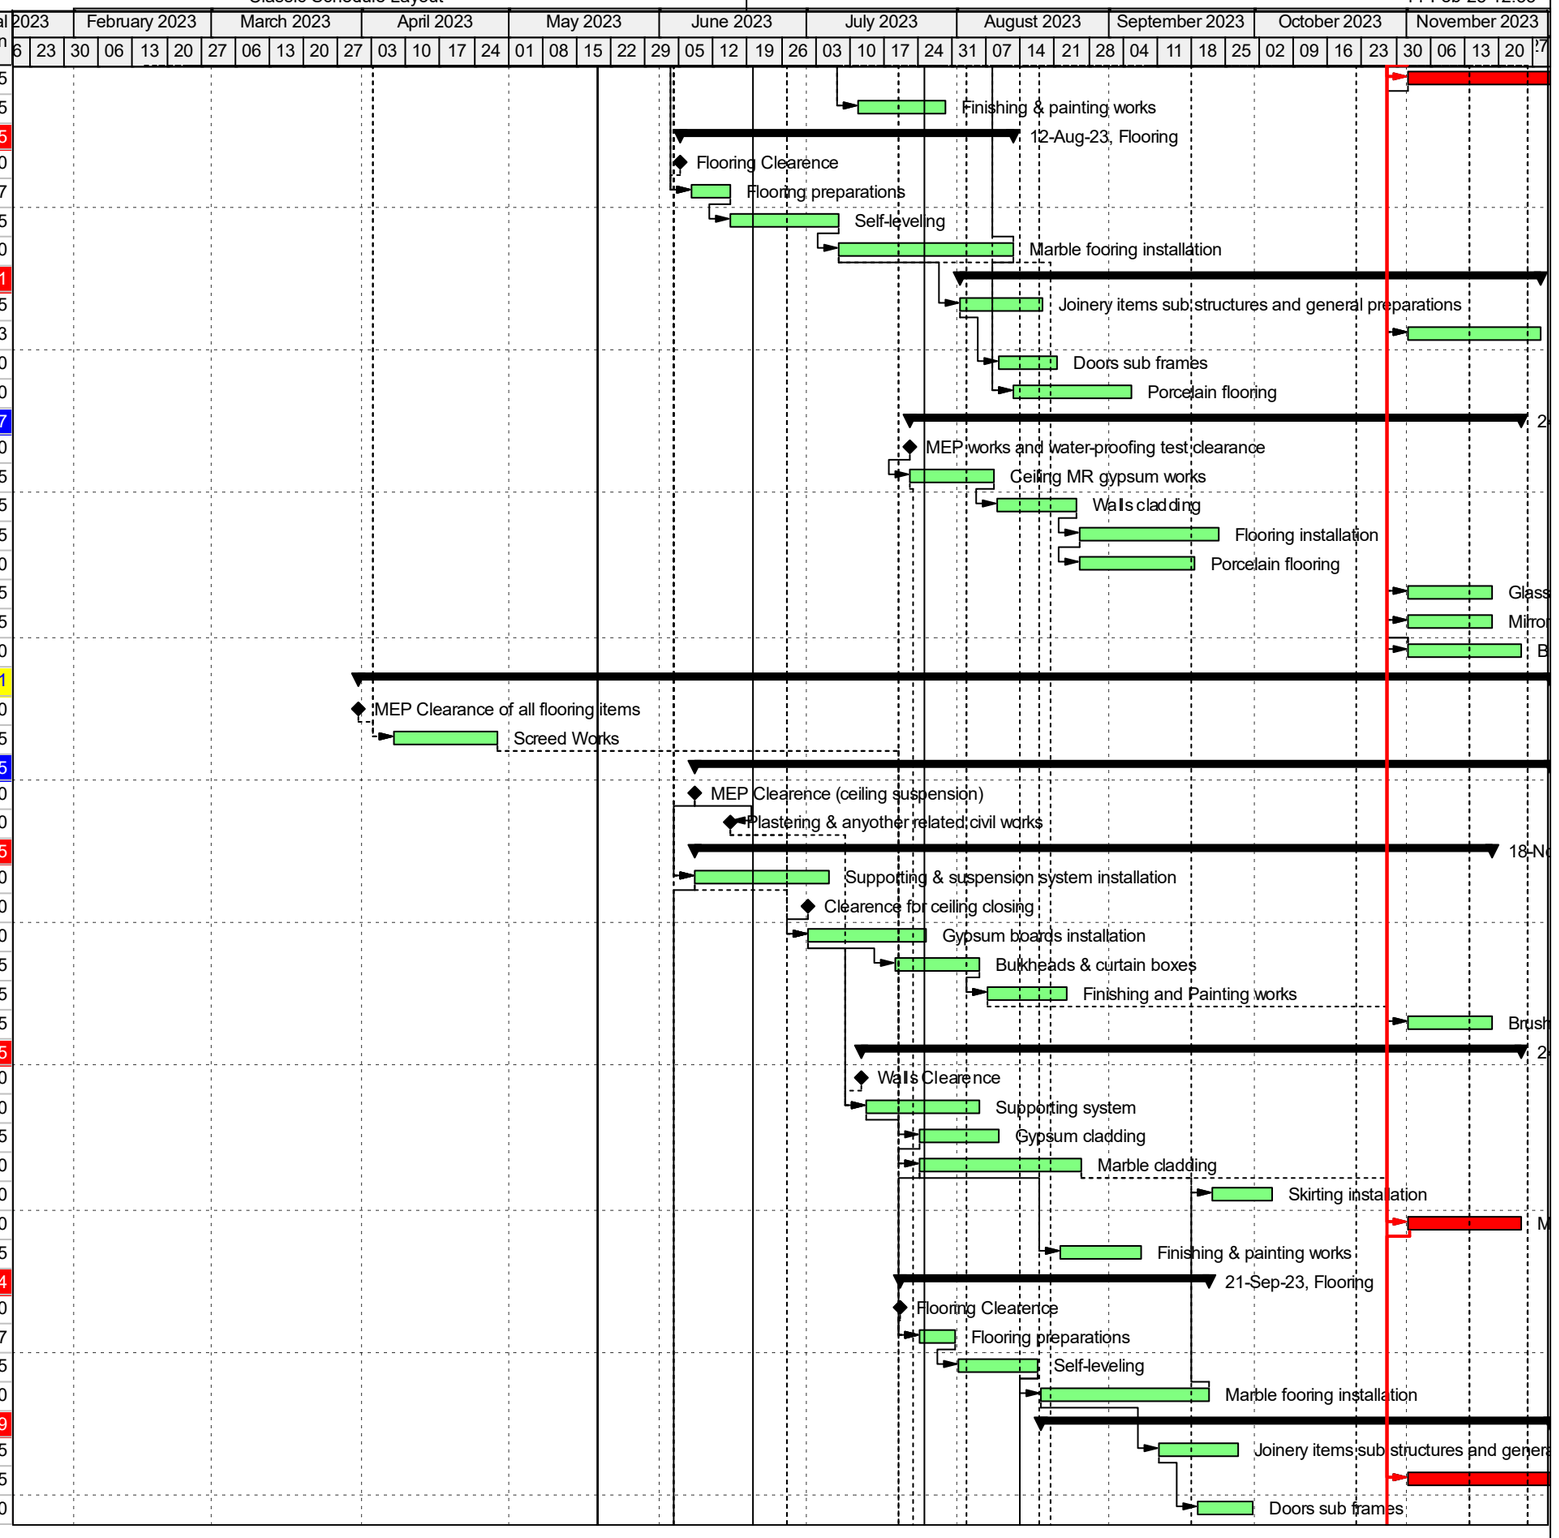

Actual Work — Remaining Work — Critical Remaining Work — Summary — Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
A5980	Porcelain flooring	18-Aug-23	21-Sep-2	30
Zone B		08-Jun-23	30-Nov-2	145
A5539	MEP Clearence (ceiling suspension)		08-Jun-23	0
A5540	Plastering & anyother related civil works		15-Jun-23	0
Ceiling		08-Jun-23	18-Nov-2	135
A5550	Supporting & suspension system installation	08-Jun-23	05-Jul-23	20
A5559	Clearence for ceiling closing		01-Jul-23	0
A5560	Gypsum boards installation	01-Jul-23	25-Jul-23	20
A5570	Bulkheads & curtain boxes	19-Jul-23	05-Aug-2	15
A5580	Finishing and Painting works	07-Aug-23	23-Aug-2	15
A5630	Brushed metal profiles installation	01-Nov-23	18-Nov-2	15
Walls		12-Jul-23	24-Nov-2	115
A5589	Walls Clearence		12-Jul-23	0
A5590	Supporting system	13-Jul-23	05-Aug-2	20
A5600	Gypsum cladding	24-Jul-23	09-Aug-2	15
A5610	Marble cladding	24-Jul-23	26-Aug-2	30
A5640	Skirting installation	22-Sep-23	04-Oct-23	10
A5650	Metal profiles installation	01-Nov-23	24-Nov-2	20
A5690	Finishing & painting works	22-Aug-23	07-Sep-2	15
Flooring		22-Jul-23	21-Sep-2	53
A5659	Flooring Clearence		22-Jul-23	0
A5660	Flooring preparations	24-Jul-23	31-Jul-23	7
A5670	Self-leveling	01-Aug-23	17-Aug-2	15
A5680	Marble fooring installation	18-Aug-23	21-Sep-2	30
Special Items & Joinery preparations		24-Jun-23	30-Nov-2	130
A5700	Joinery items sub structures and general pre	11-Sep-23	27-Sep-2	15
A5710	Mirrors installation	01-Nov-23	30-Nov-2	25
A5720	Doors sub frames	19-Sep-23	30-Sep-2	10
A5730	Parquet flooring	29-Jul-23	28-Aug-2	25
A5750	Porcelain flooring	22-Sep-23	16-Oct-23	20
A5990	Carpet flooring	24-Jun-23	05-Jul-23	5
Zone C (wet areas)		27-Jul-23	24-Nov-2	103
A5999	MEP works and water-proofing test clearanc		27-Jul-23	0
A6000	Ceiling MR gypsum works	27-Jul-23	12-Aug-2	15
A6010	Walls cladding	14-Aug-23	30-Aug-2	15
A6020	Flooring installation	31-Aug-23	16-Sep-2	15
A6030	Porcelain flooring	31-Aug-23	11-Sep-2	10
A6040	Glass partitions	01-Nov-23	18-Nov-2	15
A6050	Mirrors installation	01-Nov-23	24-Nov-2	20
A6060	Brushed metal profiles	01-Nov-23	24-Nov-2	20
Joinery & Doors		23-May-23	29-Nov-2	157
A7800	Clearance to start installaing the joinery (All		31-Jul-23	0
A7810	Clearance to strart installation the joinery (AC		31-Jul-23	0
Manufacturing		23-May-23	21-Nov-2	150
A7700	Walls cladding	23-May-23	17-Oct-23	120
A7710	Doors	23-May-23	09-Nov-2	140
A7720	Cabinets	23-May-23	21-Nov-2	150
A7730	Vanitys	23-May-23	21-Nov-2	150
A7790	Wardrobes	23-May-23	21-Nov-2	150
Installation		24-Aug-23	29-Nov-2	82
A7740	Walls cladding	24-Aug-23	27-Nov-2	80

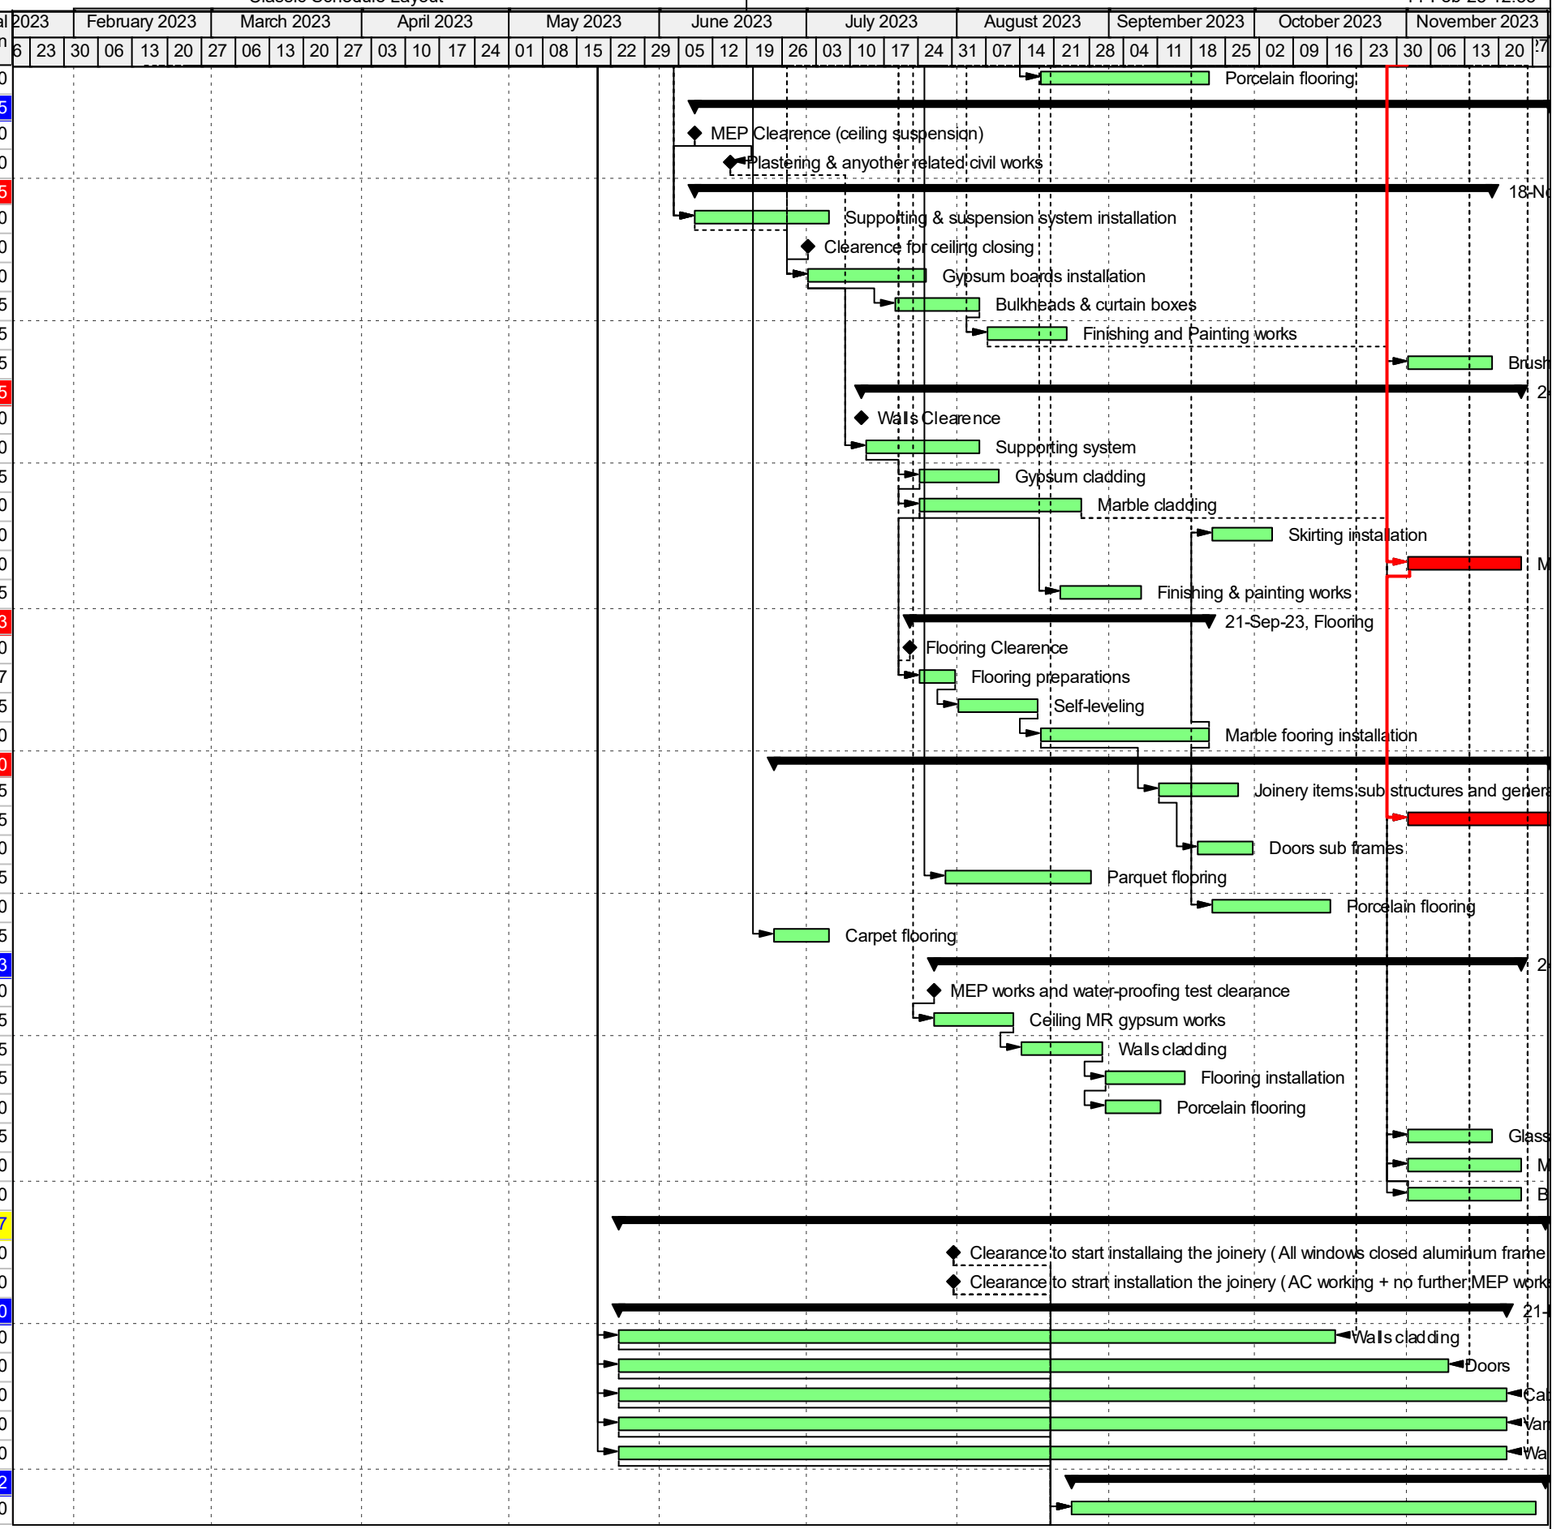

© Oracle Corporation

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration
A7750	Doors	24-Aug-23	27-Nov-2	80
A7760	Cabinets	24-Aug-23	27-Nov-2	80
A7770	Vanitys	24-Aug-23	27-Nov-2	80
A7780	Wardrobes	24-Aug-23	29-Nov-2	82



NOTE: AS per our contract the project duration is 300 days, which will be 262 working days as per the program.

© Oracle Corporation

etereo ARCHITECTURE&DESIGN&EMOTION	Eng. Adnan Saffarini Office Architects & Engineering Consultants	GUIDELINE INTERIORS

Page 1 of 1	Doc Ref.:	EAS-DT	Form sheet Title:	**Document Transmittal**

Transmittal No.	EAS-GLI-DT-001	Rev.	02	Date	Monday, 13 February 2023

Project Title	AL SAFIYA PALACE	Plot No.	0506
Employer Name	M/S AQAAR – AJMAN PROPERTIES CORPORATION	Location	AJMAN, UAE
Subject			

Transmitted to	Mr.	**From**	Mr.
Company	M/s Eng. Adnan Saffarini Office (EAS)	Company	M/s Guideline Interiors LLC
Location	Ajman Branch	Location	Dubai Silicon Oasis
Phone No.	067441101	Phone No.	043922240
Fax No.		Fax No.	043922250
Email	easajman@saffarinidxb.com	Email	projects@guideline.ae

List of Drawings / Documents Details:

Item	Drawings / Documents / Submittal Ref.	REV.	Format	No. of Copies	Description
1.	PROGRAMME OF WORK	02	Soft Copy	1	PROGRAMME OF WORK
2.	GROUND ZONE PLAN	01	Soft Copy	1	GROUND ZONE PLAN
3.	FIRST ZONE PLAN	01	Soft Copy	1	FIRST ZONE PLAN
4.	TERRACE ZONE PLAN	01	Soft Copy	1	TERRACE ZONE PLAN

Reason for Submittal

- ☐ As Requested
- ☐ For your Information & Record.
- ☑ For your Approval
- ☐ For your Comments
- ☐ Additional Copies
- ☐ For Urgent Action
- ☐ For Forwarding Sub-Contractor
- ☐ For Construction

Issued By Contractor

Name: ENGR. JOSEPH FELIX

Signature: _____

Date: 13 / 02 / 2023 Time: 10 : 20 PM/ **AM**

Received by Consultant

Name: _____

Signature: _____

Date: / / 20 Time: ____:____ PM/ AM

Consultant's Comments (Project Manager / Resident Engineer)

Approval Status:

- ☐ Approved
- ☐ Approved As noted
- ☐ Revise and Re-Submit
- ☐ Rejected

Name of Consultant's Representative:

_____

Signature: _____

Date: / / 20 Time: ____:____ PM/ AM

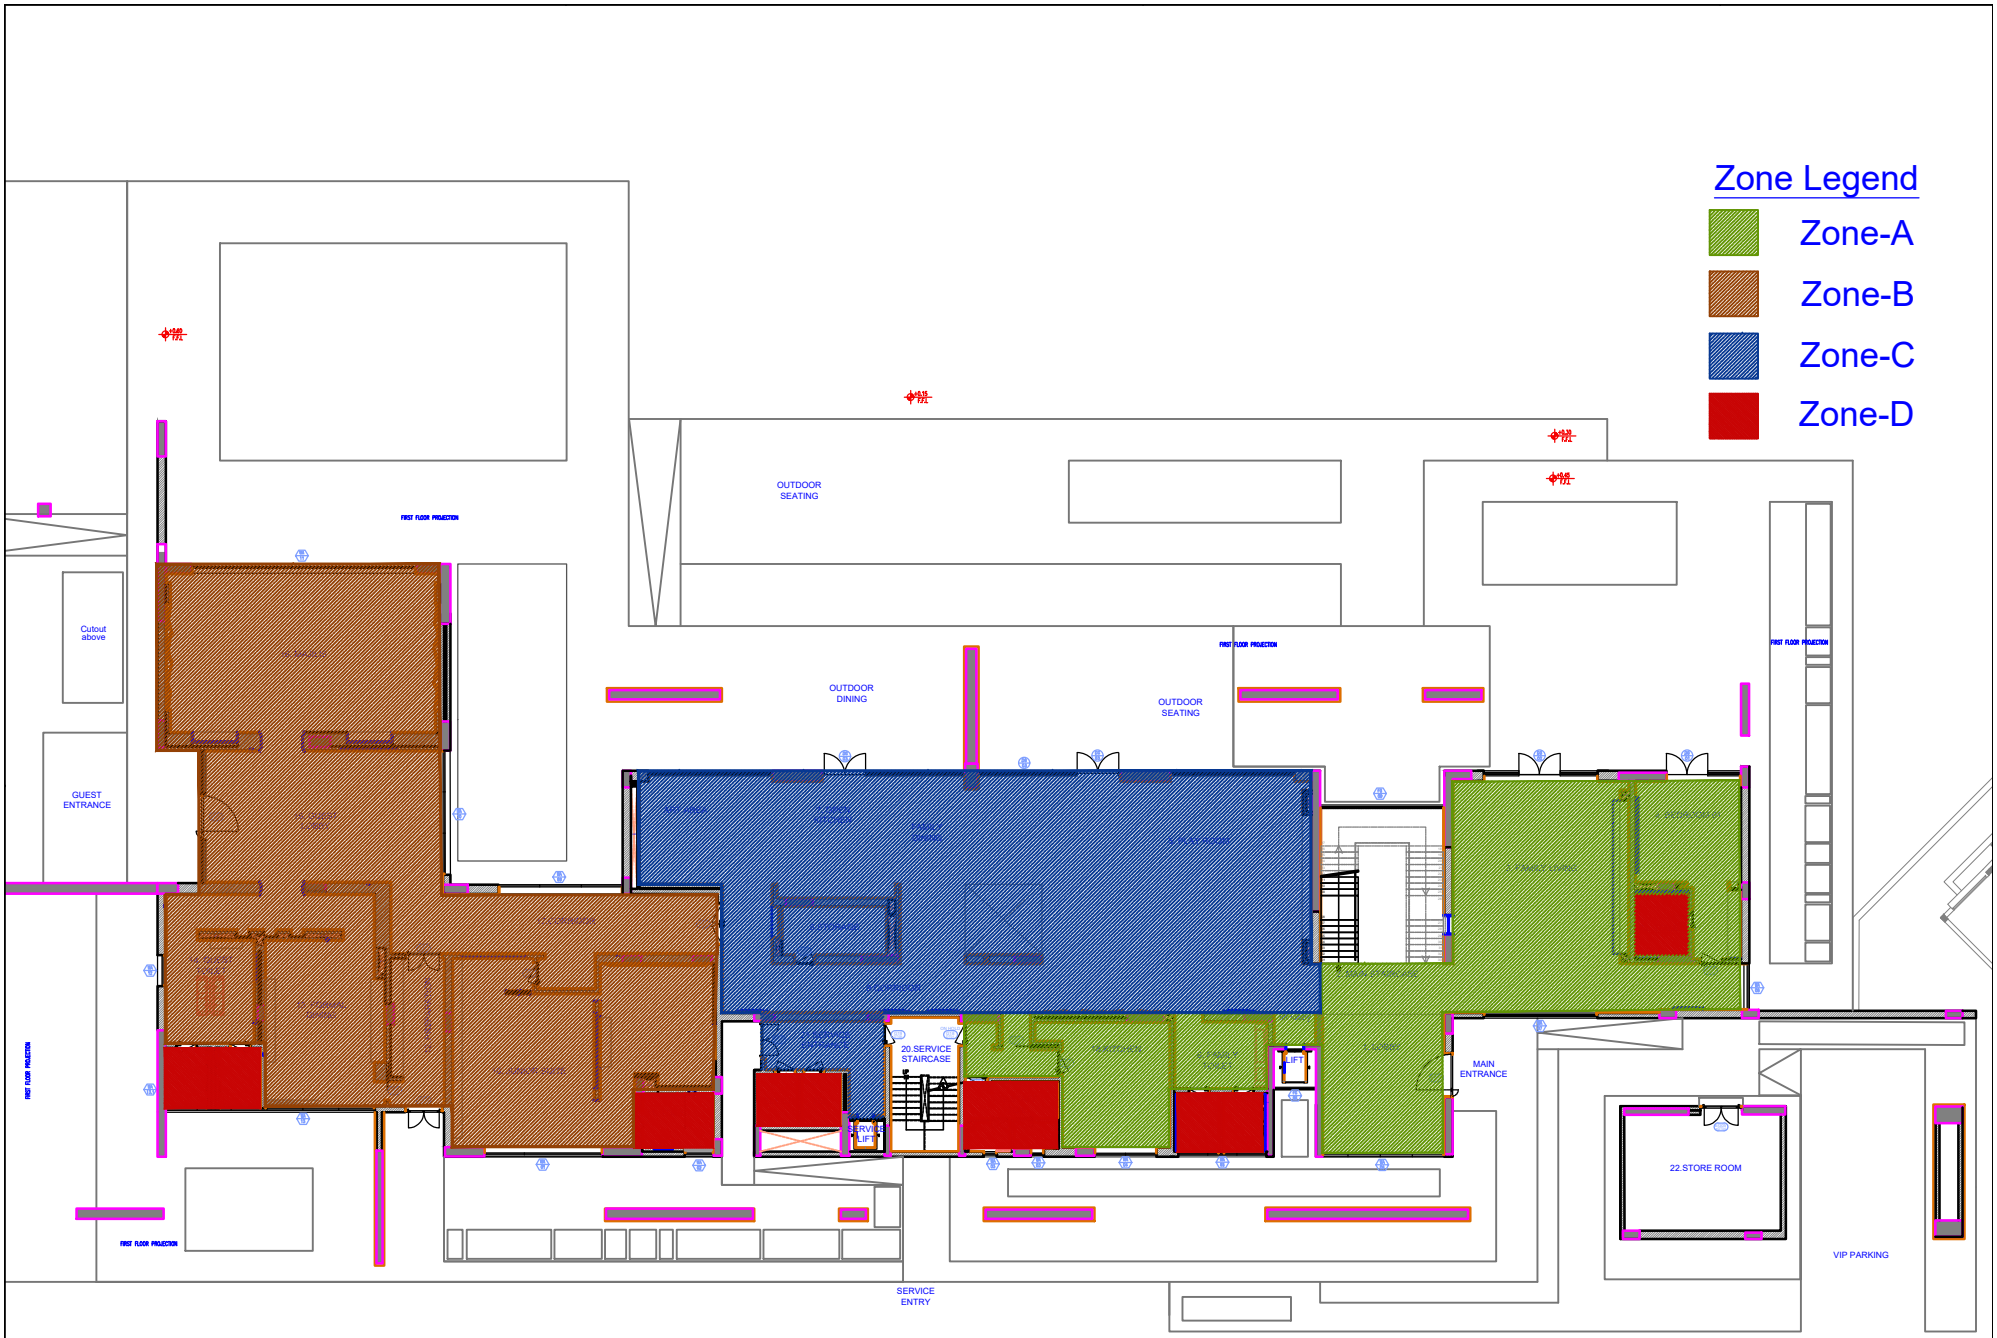

1 GROUND ZONE PLAN

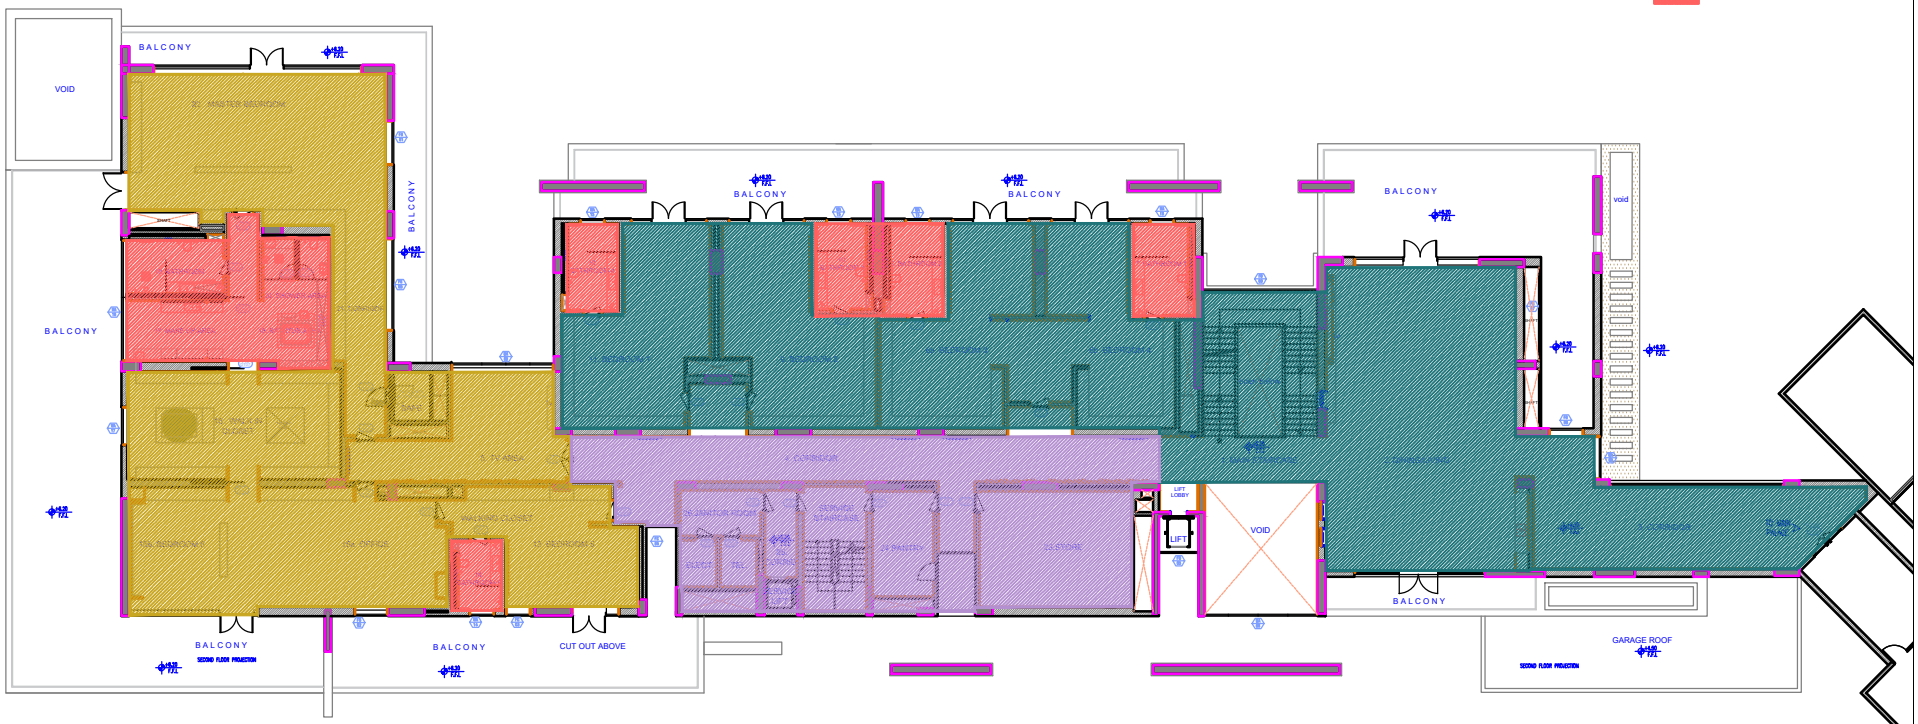

2 FIRST ZONE PLAN

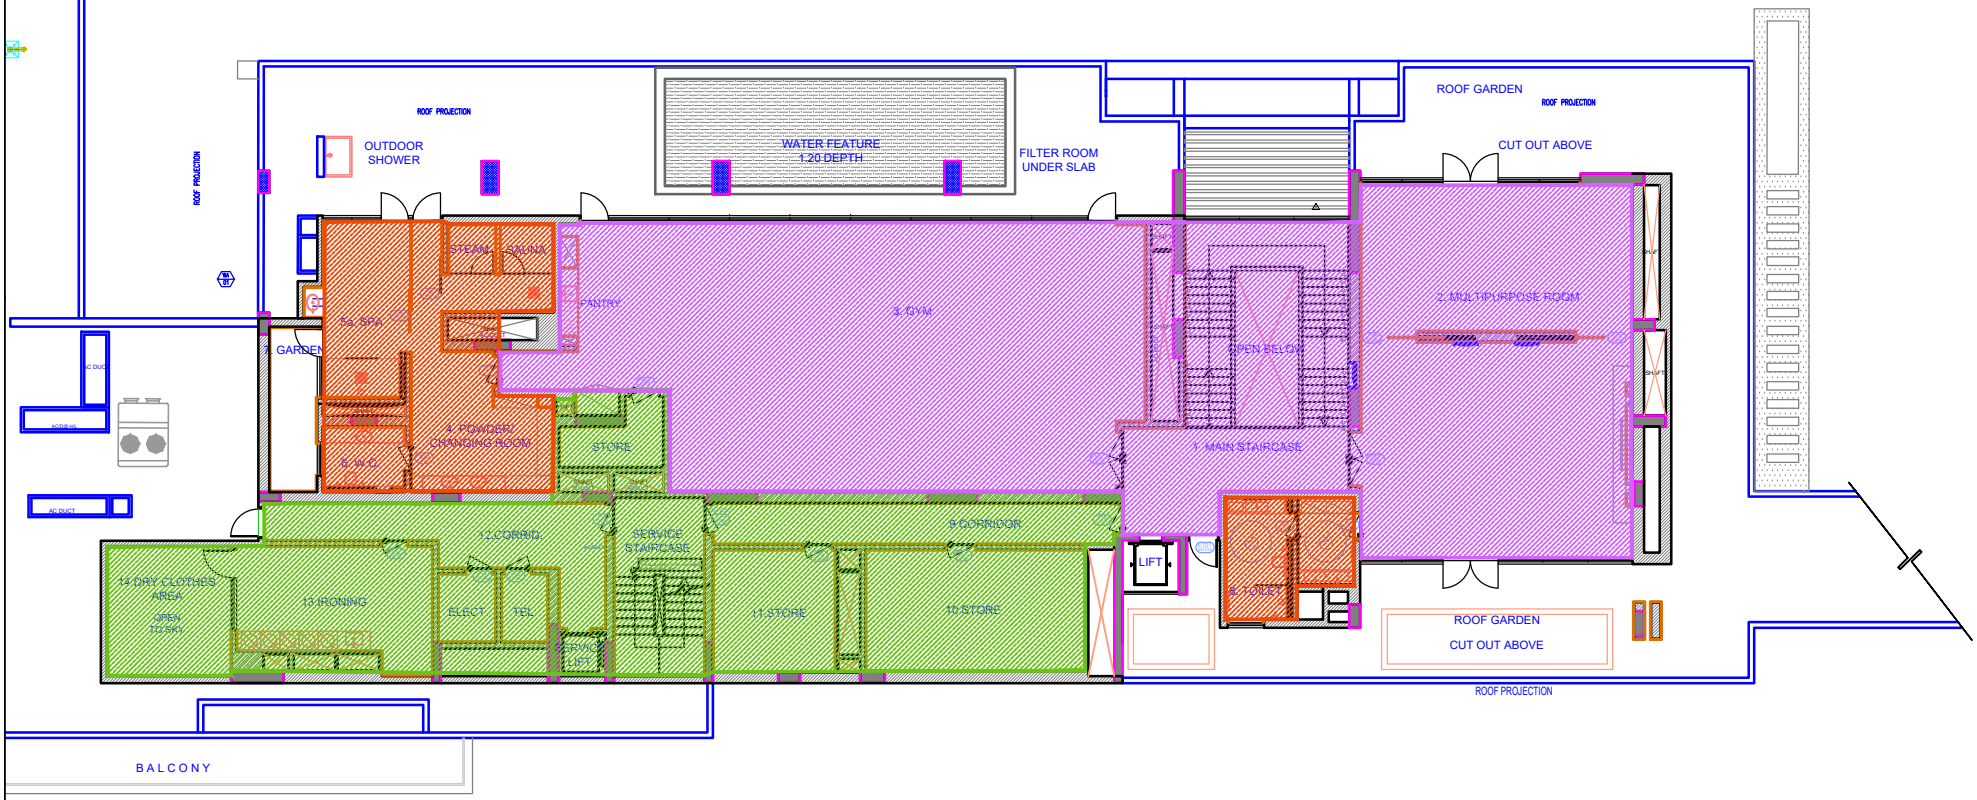

3 TERRACE ZONE PLAN
